http://www.adultpdf.com
Created by TIFF To PDF trial version, to remove this mark, please register this software.

(R - 4 - W)

(T - 19 - S)

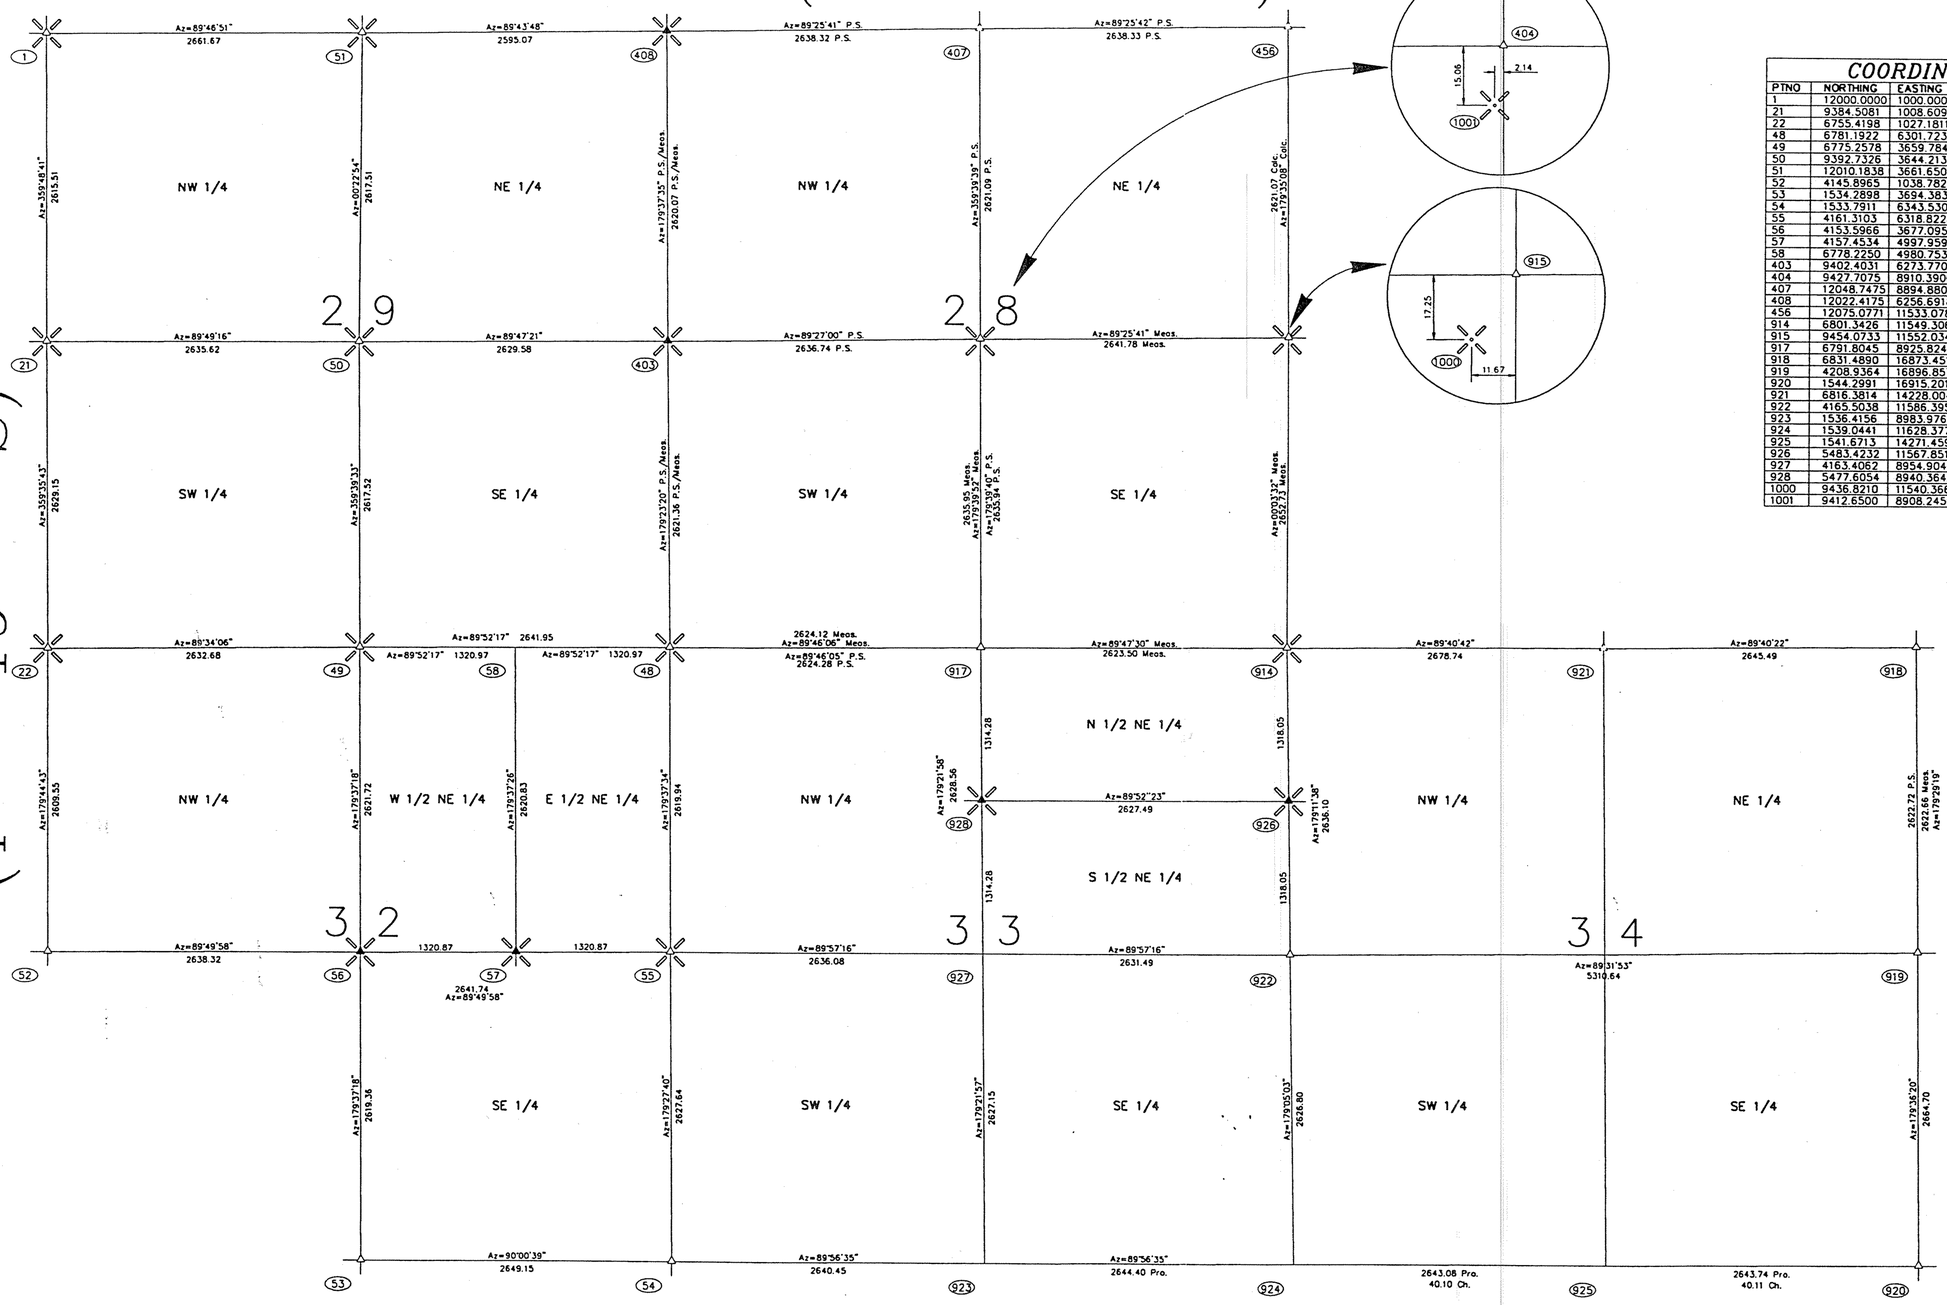

COORDINATE SCHEDULE

PTNO	NORTHING	EASTING	PANEL SET	FOUND/SET/CALC/PREVIOUS
1	12000.0000	1000.0000	YES	FOUND
21	9384.5081	1008.6099	YES	FOUND
22	6755.4198	1027.1811	YES	FOUND
48	6781.1922	6301.7230	YES	FOUND
49	6775.2578	3659.7841	YES	FOUND
50	9392.7326	3644.2137	YES	FOUND
51	12010.1838	3661.6507	YES	FOUND
52	4145.8965	1038.7829		FOUND
53	1534.2898	3694.3839		FOUND
54	1533.7911	6343.5306		FOUND
55	4161.3103	6318.8228	YES	FOUND
56	4153.5966	3677.0956	YES	SET
57	4157.4534	4997.9592	YES	SET
58	6778.2250	4980.7536	YES	CALC
403	9402.4031	6273.7705	YES	SET
404	9427.7075	8910.3900		FOUND
407	12048.7475	8894.8805		PREVIOUS
408	12022.4175	6256.6918	YES	SET
456	12075.0771	11533.0788		PREVIOUS
914	6801.3426	11549.3066	YES	FOUND
915	9454.0733	11552.0340		FOUND
917	6791.8045	8925.8243		FOUND
918	6831.4890	16873.4512		FOUND
919	4208.9364	16896.8579		FOUND
920	1544.2991	16915.2016		FOUND
921	6816.3814	14228.0041		PREVIOUS
922	4165.5038	11586.3956		FOUND
923	1536.4156	8983.9766		CALC
924	1539.0441	11628.3773		CALC
925	1541.6713	14271.4598		CALC
926	5483.4232	11567.8511		SET
927	4163.4062	8954.9046		CALC
928	5477.6054	8940.3644		SET
1000	9436.8210	11540.3669	YES	
1001	9412.6500	8908.2450	YES	

-600 0 600 1200 1800

LEGEND

- Δ - Sectional Monument Found
- ▲ - Sectional Monument Set
- - Sectional Monument Found From Previous Survey
- ┼ - Section Corner Calculated
- P.S. - Previous Survey
- M. - Measured
- Calc. - Calculated
- Pro. - Prorated
- Ch. - Chains
- - Panel Point

SURVEYOR'S CERTIFICATE:

I hereby certify this plat to be a true, correct and complete representation of the property described hereon, as surveyed under my supervision, this 6th day of October, 1999.

Daniel E. Garber RLS

Date Of Field Work: DOFW

WILLIAMS ENERGY SERVICES

CARBER SURVEYING SERVICE, P.A.

CSS 423 WEST FIRST AVENUE HUTCHINSON, KANSAS 67501 Ph. 316-665-7032 Fax 316-663-7401

SURVEY OF SECTIONS 28,29,32, 33,34,T19S, R4W McPHERSON COUNTY, KANSAS

Drawn By: WJA	Checked By: DEG
Scale: 1"=600'	Job No.: G99-656
Date: 10/06/1999	Sheet 1 of 1 Sheets
